

South Broward Hospital District Board Building Committee Construction Progress Report


Construction Services Department

April 2025

Joe DiMaggio Children's Hospital

CT Replacement


- Scope of Work: Replace CT & RF equipment and switch existing rooms in order to minimize equipment down time
- Status of Project: Bidding
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Harvard Jolly Inc.
- Contractor: TBD
- Board Approval Date: June 2025
- Cost of Construction: Estimated \$900,000
- Total Estimated Cost: Estimated \$4,500,000

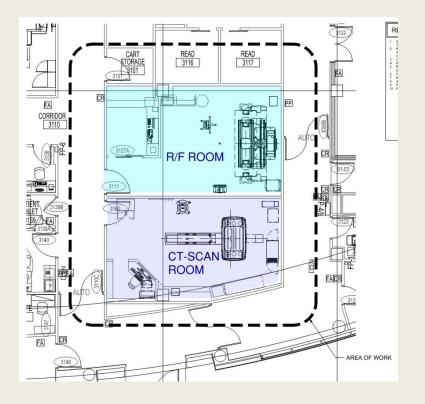


Joe DiMaggio Children's Hospital

JDCH Building Commissioning Mechanical Issues

- Scope of Work: Mechanical equipment and code updates
- Status of Project: Bidding
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Akin Brooks Engineering
- Contractor: TBD
- Board Approval Date: June 2025
- Cost of Construction: \$705,000.00
- Total Estimated Cost: \$1.5M

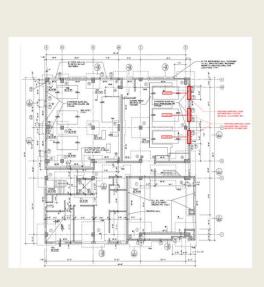




Memorial Healthcare System

MHS 7029-7031 Taft Community Youth Services Renovation

- Scope of Work: Replacement of Interior Finishes at 7029 and 7031 Suites
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Gresham Smith
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: \$1,790,000
- Total Estimated Cost: \$3,652,000






Memorial Healthcare System

UCC 10175 Pines Blvd

- Scope of Work: Interior renovation of Chase bank for outpatient services
- Status of Project: Permitting/Land use approval
- Schedule Completion: TBD
- Current Status: Impacted
- Comments: Pending County approval for plat note amendment
- Architect: Saltz Michelson Architects
- Contractor: LEE Construction Group
- Board Approval Date: July 24, 2024
- Cost of Construction: \$2.99M
- Total Estimated Cost: \$4.0M

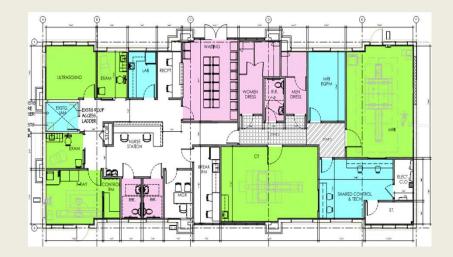

Memorial Healthcare System

MHS IT Data Center ASCO Equipment

- Scope of Work: Replace electrical switchgear serving the data center.
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Gresham Smith
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: TBD
- Total Estimated Cost: \$1M





Memorial Hospital Miramar

Monument Sign Replacements

- Scope of Work: Exterior sign replacement 49 signs total
- Status of Project: Construction
- Schedule Completion: September 2025
- Current Status: On Schedule
- Architect: Harvard Jolly Inc.
- Contractor: LEE Construction Group
- Board Approval Date: March 27, 2024
- Cost of Construction: \$1,987,615
- Total Estimated Cost: \$2,186,000










Memorial Hospital Miramar

MHM Ultrasound X-Ray Room Relocation/ED Overflow

- Scope of Work: Replacement of Xray machine. New ultrasound and exam rooms. Create a decontamination room. Additional offices. Upgrade finishes.
- Status of Project: Permitting/Bidding
- Schedule Completion: TBD
- Current Status: Permitting/Bidding
- Architect: Harvard Jolly Inc.
- Contractor: Lee Construction
- Board Approval Date: April 23, 2025
- Cost of Construction: \$1,502,130
- Total Estimated Cost: \$2,200,000





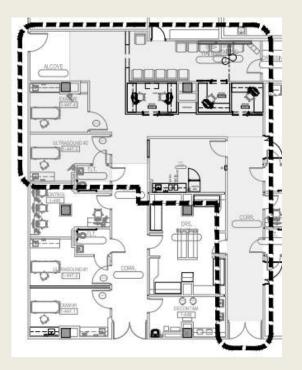


Memorial Hospital Miramar

MOB 2 MRI/CT Lab

- Scope of Work: Build-out of 3,956 SF of existing 1st floor shell space. New functions include MRI room, CT scan room, lab infusion and patient and Staff support spaces
- Status of Project: Construction
- Schedule Completion: January 2026
- Current Status: In progress
- Architect: Harvard Jolly Inc.
- Contractor: LEE Construction Group
- Board Approval Date: July 24, 2024
- Cost of Construction: \$3.1M
- Total Estimated Cost: \$12.3M



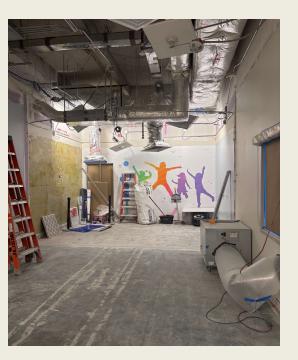

MHP Roof Replacement

- Scope of Work: Replace 92,500 SF exterior roof
- Status of Project: Permitting
- Schedule Completion: TBD
- Current Status: Pending Permit
- Comments: Bid awarded
- Architect: Harvard Jolly Inc.
- Contractor: Lego Construction Company
- Board Approval Date: January 20, 2025
- Cost of Construction: \$4.8M
- Total Estimated Cost: \$7.7M



Douglas Road Free Standing ED

- Scope of Work: 30,000 SF new construction of a Free-Standing Emergency Department
- Status of Project: Construction
- Schedule Completion: July 2026
- Current Status: On Schedule
- Architect: HKS Architects Inc.
- Contractor: DPR Construction
- Board Approval Date: October 24, 2024
- Cost of Construction: \$38.5M
- Total Estimated Cost: \$52.85M





Red Road Free Standing ED

- Scope of Work: 17,000 SF new construction Free Standing Emergency
 Department
- Status of Project: Construction
- Schedule Completion: April 2026
- Current Status: On Schedule
- Architect: HKS Architects Inc.
- Contractor: DPR Construction
- Board Approval Date: October 24, 2024
- Cost of Construction: \$23.4M
- Total Estimated Cost: \$34.8M






MHP MRI Replacement

- Scope of Work: New MRI Suite to replace the existing MRI Modular Unit nearing end of life. Relocate existing rooms to accommodate new MRI Suite.
- Status of Project: Planning
- Schedule Completion: TBD
- Current Status: Preliminary planning
- Comments: In planning
- Architect: Harvard Jolly Inc.
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: Estimated \$5.81M
- Total Estimated Cost: \$9.65M



Envelope Repairs

- Scope of Work: Repair exterior envelope to prevent water intrusion, replace windows as needed
- Status of Project: Hold
- Schedule Completion: TBD
- Current Status: TBD
- Architect: Harvard Jolly Inc.
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: TBD
- Total Estimated Cost: \$10.6M

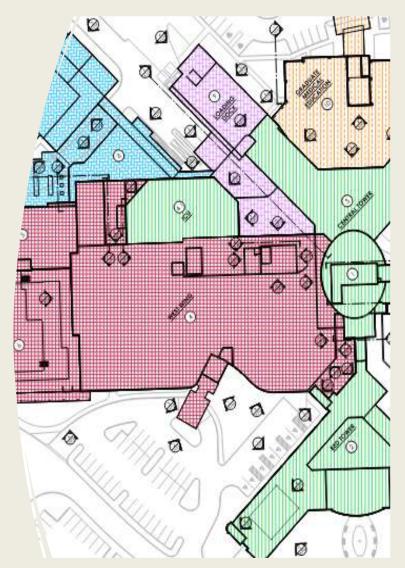


Memorial Hospital West Garage Restoration

- Scope of Work: Structural Restoration of Parking Garage A, B, & C. Project will be completed in multiple phasing to help maintain traffic flow throughout the garages.
- Status of Project: Permitting
- Schedule Completion: TBD
- Current Status: On Schedule
- Engineer: Kimley-Horn & Associates
- Contractor: Engel Construction
- Board Approval Date: February 27, 2025
- Cost of Construction: \$2,098,122
- Total Estimated Cost: \$4.0M




MHW IR Room #2 Equipment Replacement


- Scope of Work: IR Equipment replacement and room finishes
- Status of Project: Permitting/Bidding
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Gresham Smith
- Contractor: TBD
- Board Approval Date: June 2025
- Cost of Construction: Estimated \$1,000,000
- Total Estimated Cost: \$2,610,000

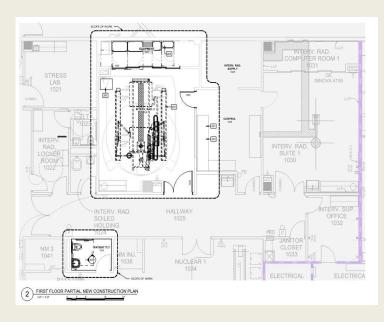

MHW CT Scan Room

- Scope of Work: Move existing CT scan to current ultrasound room and replace CT equipment
- Status of Project: Permitting/Bidding
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Gresham Smith
- Contractor: TBD
- Board Approval Date: June 2025
- Cost of Construction: Estimated \$1,400,000
- Total Estimated Cost: \$3,921,000

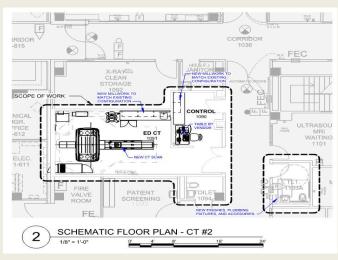



2nd Floor Labor & Delivery


- Scope of Work: Interior Renovation upgrade for existing 14 rooms, (6) triage rooms, (1) exam room, nurse's station, and upgraded amenities.
- Status of Project: Construction
- Schedule Completion: May 2025
- Current Status: Unforeseen
- Architect: HKS Architects Inc.
- Contractor: LEE Construction Group
- Board Approval Date: February 28, 2024
- Cost of Construction: \$2,768,050
- Total Estimated Cost: \$9,592,689





MHW CVI #2 Equipment Replacement

- Scope of Work: New Cath Lab Equipment in Room #2 with finish renovations, Reading Room enlargement, and required changes to MEP
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Gresham Smith
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: \$1.9M
- Total Estimated Cost: \$4.3M

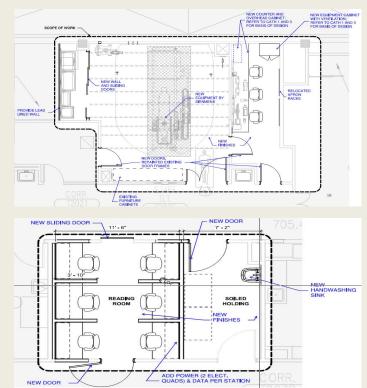


MHW Elevator 1-2 Modernization

- Scope of Work: Modernization of elevators 1 & 2 in front lobby
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Cost of Construction: TBD
- Total Estimated Cost: \$2.4M








MHW MRI Upgrade


- Scope of Work: Upgrade MRI components and associate equipment, including chiller unit, Liebert unit, electrical panel, etc. to enable the renovations. A temporary MRI Trailer will be set up at the existing adjacent exit previously used for a temporary imagining trailer.
- Status of Project: Construction
- Schedule Completion: August 2025
- Current Status: On Schedule
- Architect: Harvard Jolly Inc.
- Contractor: LEE Construction Group, Inc.
- Board Approval Date: September 25, 2024
- Cost of Construction: \$912,030
- Total Estimated Cost: \$2,888,000






MHW MCVI West

- Scope of Work: Renovation of existing building to accommodate MCVI functionality including CT and Nuclear CT.
- Status of Project: Construction
- Schedule Completion: October 2025
- Current Status: On Schedule
- Architect: Harvard Jolly Inc.
- Contractor: LEE Construction Group
- Board Approval Date: December 4, 2024
- Cost of Construction: \$5.7M
- Total Estimated Cost: \$14.5M

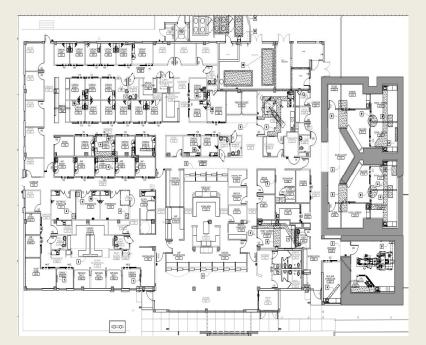

MHW MCI Infusion Expansion

- Scope of Work: Tenant improvement design to infill existing 5,160 SQ FT shell with infusion bays, exam rooms, offices and restrooms
- Status of Project: Permitting
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: HKS Architects Inc.
- Contractor: Thornton Construction, Inc.
- Board Approval Date: February 27, 2025
- Cost of Construction: \$1,984,552
- Total Estimated Cost: \$9,000,000

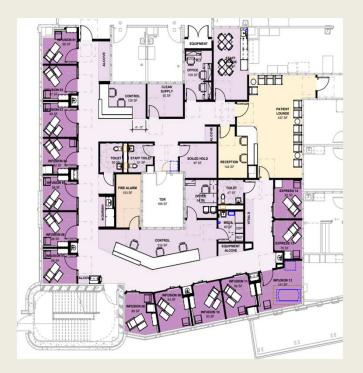

Memorial Manor

Manor Generator/ATS Replacement


- Scope of Work: Replacement of generator and automatic transfer switch
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: TBD
- Total Estimated Cost: \$3.51M



Memorial Manor

Manor Piped-in O2

- Scope of Work: Replace existing oxygen tank farm with an upgraded system to meet current codes, including upgrades to the existing tank slab and enclosure. Install (1) new oxygen station at (25) existing patient beds and a new emergency oxygen connection that would serve as a backup.
- Status of Project: Permitting/Bidding
- Schedule Completion: TBD
- Comments: In Bidding
- Architect: HKS Architects Inc.
- Contractor: TBD
- Board Approval Date: May 2025
- Cost of Construction: \$3.0M
- Total Estimated Cost: \$3.8M

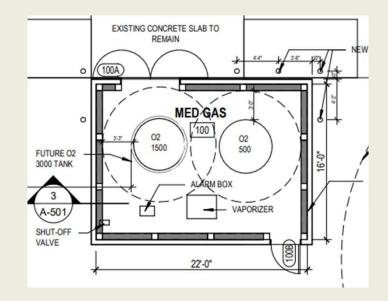

Memorial Manor

Manor FEMA Hardening


- Scope of Work: Exterior hurricane hardening of 1-story nursing home. Work includes reinforcing existing exterior non-reinforced concrete block walls, reinforcing existing roof trusses, replacing plywood over roof trusses, structural enhancements at gable ends, new metal roof, doors, windows and louvers.
- Status of Project: Permitting
- Schedule Completion: TBD
- Current Status: TBD
- Architect: Saltz Michelson Architects
- Contractor: LEE Construction Group
- Board Approval Date: February 27, 2025
- Cost of Construction: \$4,217,850.00
- Total Estimated Cost: \$7.0M



Memorial Physicians Group

MHM MOB Suite 309 Maternal Fetal Medicine


- Scope of Work: Renovation of existing 2,675 SF suite for Maternal Fetal Medicine office.
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: Estimated \$660,000
- Total Estimated Cost: \$1.55M

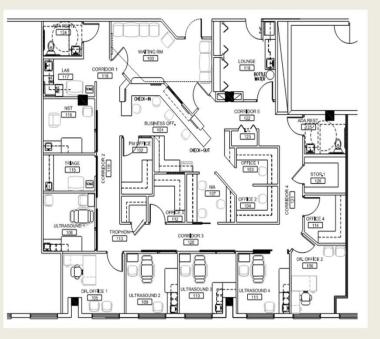

Memorial Physicians Group

MPG MHW 603 Ste 250 Division of Urology

- Scope of Work: Tenant interior buildout to accommodate new medical facilities inclusive of Urology medical practice, (7) exam rooms and (4) procedure rooms.
- Status of Project: Permitting/Bidding
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: June 2025
- Cost of Construction: \$1,123,500
- Total Estimated Cost: \$2,093,101

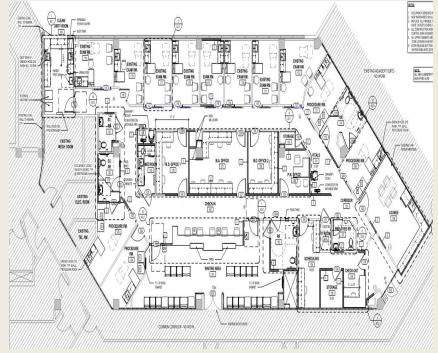

Memorial Primary Care-Regional

Buildout Dania Beach Center

- Scope of Work: Build out of shell space 4,680 sf to include: 15 exam rooms; 5 Providers (3 PCP and 2 Specialty); 5 PFSRs (at check in/check out); 6 Mas; 1 Office Practice manager/ Shared by PG and PC
- Status of Project: Construction
- Schedule Completion: May 2025 (1 Month Early)
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: LEE Construction Group
- Board Approval Date: March 27, 2024
- Cost of Construction: \$1,915,242
- Total Estimated Cost: \$3.12M









MCI Hallandale Expansion

- Scope of Work: Expand existing MCI Hallandale clinic to add (11) infusion bays, (7) exam rooms and support spaces
- Status of Project: Bidding
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Harvard Jolly Inc.
- Contractor: TBD
- Board Approval Date: May 2025
- Cost of Construction: TBD
- Total Estimated Cost: \$15.249M

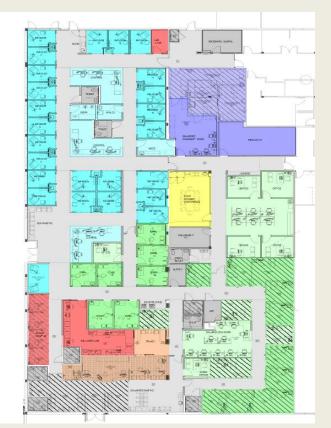


MRH Bi-Plane Upgrade (Neuro CVI)

- Scope of Work: Equipment replacement of Neuro Bi-Plane Hybrid OR
- Status of Project: Permitting
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Gresham Smith
- Contractor: LEE Construction Group
- Board Approval Date: February 27, 2025
- Cost of Construction: \$758,625
- Total Estimated Cost: \$3.502M

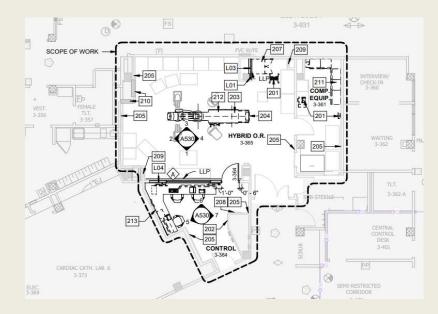


MRH Therapy Room #1 Linac Replacement

- Scope of Work: Replacement of the existing MRH Linear Accelerator equipment in Therapy Room #1, finishes and cabinetry
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: TBD
- Total Estimated Cost: \$5.334M

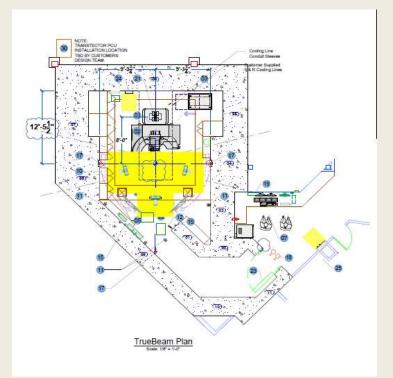


MRH Service Elevators 1-2-3

- Scope of Work: Modernization of elevators 1-2-3
- Status of Project: Permitting/Bidding
- Schedule Completion: TBD
- Comments: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: N/A
- Cost of Construction: TBD
- Total Estimated Cost: \$1,800,000

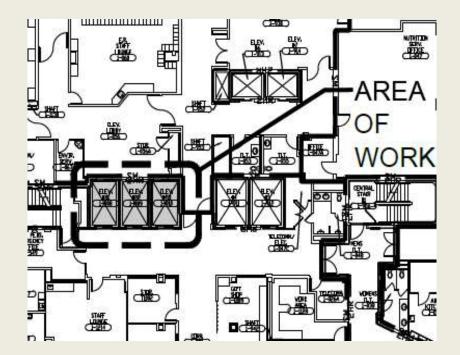

Memorial Regional Hospital MRH Kidney Transplant Clinic

- Scope of Work: 18,800 SF renovation relocating Transplant Services to Venture Corporate Center to improve patient access
- Status of Project: Construction
- Schedule Completion: October 2025
- Current Status: On Schedule
- Architect: Harvard Jolly Inc.
- Contractor: Landlord Fit-Out
- Board Approval Date: January 20, 2025
- Cost of Construction: \$1,819,793.00
- Total Estimated Cost: \$4.372M

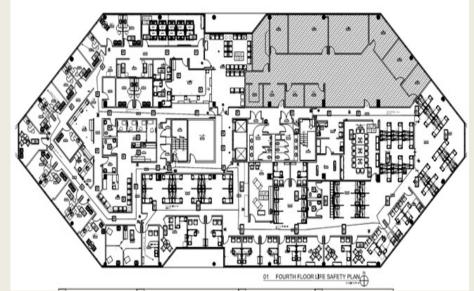

Memorial Regional Hospital ER Renovation

- Scope of Work: MRH ED Interior Finishes. Full interior finish renovation including flooring, wall covering, doors, ceiling, restrooms with plumbing fixtures, nursing station replacement, casework, etc. (35,049 SF). 1,200 SF of new construction to accommodate decontamination showers and exam room, expanded storage, and improved EMS lounge. Additionally, the project involves 4,500 SF of renovations to improve the layout, efficiency and patient access within the existing 3 trauma bays and resuscitation room 5,700 SF
- Status of Project: Construction
- Schedule Completion: December 2025
- Current Status: Revised schedule due to phasing and unforeseen
- Comments: Phase 1 and 2 of Trauma completed March 7, 2025
- Architect: Harvard Jolly Inc.
- Contractor: Turner Construction
- Board Approval Date: May 25, 2022
- Cost of Construction: \$16.4M
- Total Estimated Cost: \$25.1M







MRH Chiller Replacement

- Scope of Work: Chiller replacement planned by MRH including electrical and plumbing upgrades.
- Status of Project: Planning
- Schedule Completion: TBD
- Current Status: On Schedule
- Engineer: Davila Engineering
- Contractor: TBD
- Board Approval Date: TBD
- Cost of Construction: \$700K
- Total Estimated Cost: \$1.6M






Master Plan Surgery and Tower

- Scope of Work: Build new 8-story patient and surgical tower with 3-story connector. Scope includes interior renovation of several areas on the 1st and 2nd floors (Main lobby, Registration, Heart Clinic, OR Suite, SPD, Material Management, etc.) Upgrade existing MEP infrastructure to support new spaces
- Status of Project: Permitting/Bidding
- Schedule Completion: TBD
- Comments: Pending workshop
- Architect: HKS Architects Inc.
- Contractor: Robins & Morton
- Board Approval Date: Expected June 2025
- Cost of Construction: TBD
- Total Estimated Cost: \$750M



MRHS Pedestrian Bridge Restoration

- Scope of Work: Pedestrian bridge structural restoration.
- Status of Project: Permitting
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Kimley-Horn & Associates
- Contractor: Lego Construction Company
- Board Approval Date: February 27, 2025
- Cost of Construction: \$1,688,315.20
- Total Estimated Cost: \$2,100,000

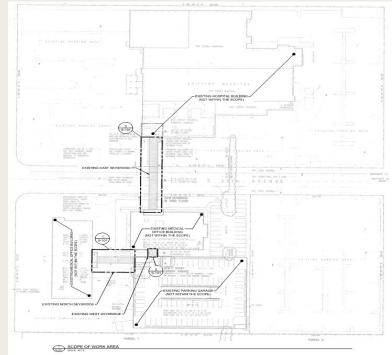


Chiller 3 Replacement


- Scope of Work: Replace Chiller #3 and associated cooling tower with new equipment in the same location
- Status of Project: Construction
- Schedule Completion: June 2025
- Current Status: On Schedule
- Comments: New chiller and cooling tower are in operation
- Architect: Saltz Michelson Architects
- Contractor: LEE Construction Group
- Board Approval Date: April 26, 2023
- Cost of Construction: \$1.456M
- Total Estimated Cost: \$2.603M



MRHS CT Imaging Suite Addition


- Scope of Work: The project consists of converting existing Ultrasound space for a new CT Scan Room and control room. The scope requires reconfiguration of the existing Nuclear medicine for (3) new Ultrasound rooms. Additionally, merging imaging and surgery waiting area and cosmetic upgrade for ED waiting area.
- Status of Project: Permitting/Bidding
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Harvard Jolly Inc.
- Contractor: TBD
- Board Approval Date: June 2025
- Cost of Construction: Estimated \$2,500,000
- Total Estimated Cost: \$5,544,000





HVAC AHU 3

- Scope of Work: Replacement of AHU-3
- Status of Project: Design
- Schedule Completion: TBD
- Current Status: On Schedule
- Architect: Saltz Michelson Architects
- Contractor: TBD
- Board Approval Date: June 2025 (tentative)
- Cost of Construction: TBD
- Total Estimated Cost: \$2.198M

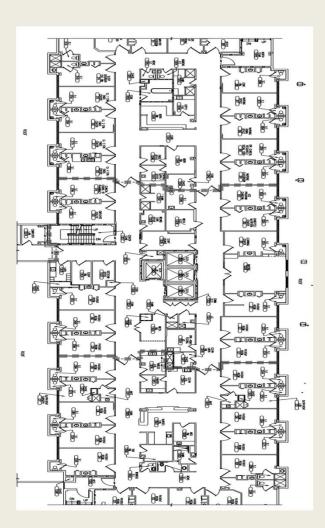

MRHS Remediation

- Scope of Work: Remediation of the East & West tower facade to mitigate moist air entering the building
- Status of Project: Planning
- Schedule Completion: TBD
- Comments: Working with design team to refine scope of work.
- Architect: HKS Architects Inc.
- Contractor: Thornton Construction
- Board Approval Date: TBD
- Cost of Construction: TBD
- Total Estimated Cost: \$4.3M





								South Broward Hospita Board Building Comm Construction Progress I	ittee								
Project	Status	Contractor	Architect	Budget LTD	Prior Years Expenses	Current FY25	Obligations	April-25 Funds Remaining	Approved Contractor Bid Amount	Approved Contingency Amount	On Budget	Contract Type	Board Approval Date	Construction Start Date	Original Construction Completion Date	On Schedule?	Comments
pe DiMaggio Children's Hospital - 46		1															
CT Replacement	Design	TBD	HARVARD JOLLY INC	4,600,000.00	-	56,725.00	2,335,725.90	2,207,549.10	TBD	TBD	TBD	Bid	June (Tentative)	TBD	TBD	TBD	TBD
JDCH Building Commissioning Mechanical Issues	Permitting/Bidding	TBD	AKIN BROOKS ENGINEERING	1.509.990.00	148.889.30	114,934.99	12,800.00	1,233,365.71	TBD	TBD	TBD	Bid	June (Tentative)	TBD	TBD	TBD	TBD
emorial Healthcare System - 10			-				-										
MHS 7029-7031 Taft Community Youth Services Renovation*	Design	TBD	GRESHAM SMITH	1,443,800.00	-	267,921.60	209,751.40	966,127.00	TBD	TBD	TBD	Bid	TBD	TBD	TBD	TBD	TBD
UCC 10175 Pines Blvd*	Permitting/Bidding	LEE CONSTRUCTION	SALTZ MICHELSON ARCHITECTS	4.000.000.00	123.393.86	81.237.26	158.714.46	3,636,654.42	2,188,200.00	328,230.00	TBD	Bid	07/24/2024	TBD	TBD	Yes	Unforeseen Condi
MHS IT Data Center ASCO Equipment	Design	TBD	GRESHAM SMITH					541,042.00	TBD	TBD	TBD	Bid	TBD	TBD	TBD	TBD	TBD
emorial Hospital Miramar - 45												1					
Monument Sign Replacements* IHM Ultrasound Xray Room Relocation / ED	Permitting/Bidding	LEE CONSTRUCTION	HARVARD JOLLY INC	2.092.000.00	131.332.50	556.342.10	1.363.727.46	40,597.94	1,728,615.00	259,000.00	Yes	Bid	03/27/2024	12/10/2024	09/30/2025	Yes	On Schedul
Overflow*	Permitting/Bidding	LEE CONSTRUCTION	HARVARD JOLLY INC	1,389,500.00		50,345.93	573,254.58	765,899.49	1,306,200.00	195,930.00	Yes	Bid	04/23/2025	TBD	TBD	TBD	TBD
MOB2 MRI/CT Lab*	Construction	LEE CONSTRUCTION	HARVARD JOLLY INC	9 400 000 00	66.840.00	130 248 72	8 500 036 93	702,874.35	3,140,550.00	471,000.00	Yes	Bid	07/24/2024	TBD	01/30/2026	Yes	On Schedule
emorial Hospital Pembroke - 44																	
MHP Roof Replacement*	Permitting/Bidding	LEGO CONSTRUCTION	HARVARD JOLLY INC	1,350,000.00	-	98.40	428,066.53	921,835.07	3,840,661.65	768,132.00	No	Bid	01/20/2025	TBD	TBD	TBD	TBD
Douglas Road Free Standing ED*	Construction	DPR CONSTRUCTION	HKS ARCHITECTS INC	52,852,300.00	1,616,932.05	443,813.18	6,996,381.70	43,795,173.07	38,449,952.00	1,088,206.00	Yes	GMP	10/24/2024	03/10/2025	07/17/2026	Yes	On Schedule
Red Road Free Standing ED* MHP MRI Replacement*	Construction Planning	DPR CONSTRUCTION TBD	HKS ARCHITECTS INC HARVARD JOLLY INC	0.005				29,134,219.08 3,000,000.00	23,358,673.00 TBD	661,095.00 TBD	Yes TBD	GMP Bid	10/24/2024 TBD	03/03/2025 TBD	04/17/2026 TBD	Yes	On Schedule On Schedule
				3.000.000.00	-		-			.=					.=		
emorial Hospital West - 43	Hold	TBD	HARVARD JOLLY INC					3,107,914.05	TBD	TBD	TBD	GMP	TBD	TBD	TBD	TBD	TBD
Envelope Repairs*		ENGEL	KIMLEY HORN AND	3,487,700.00	182,196.00	20,244.00	177,345.95										
MHW Parking Garage Restoration	Permitting/Bidding	CONSTRUCTION	ASSOCIATES INC	2.098.122.00				-	2.098.122.00	314,000.00	TBD	Bid	02/27/2025	TBD	TBD	TBD	TBD
IHW IR Room #2 Equipment Replacement*	Design	TBD	GRESHAM SMITH	250,000.00	-	62,900.00	41,730.00	145,370.00	TBD	TBD	TBD	Bid	June (Tentative)	TBD	TBD	TBD	TBD
MHW CT Scan Room*	Design	TBD	GRESHAM SMITH	2.186.500.00		83.277.00	1.725.099.16	378,123.84	TBD	TBD	Yes	Bid	June (Tentative)	TBD	TBD	TBD	TBD
2nd Floor Labor & Delivery	Construction	LEE CONSTRUCTION	HKS ARCHITECTS INC	10,779,700.00	410,321.08	3,465,247.51	1,880,931.56	5,023,199.85	2,768,050.00	415,200.00	Yes	Bid	02/28/2024	08/12/2024	04/28/2025	05/28/2025	Unforseen Cond
MHW CVI #2 Equipment Replacement	Design	TBD	GRESHAM SMITH		410,321.00			2,373,384.00	TBD	TBD	TBD	Bid	TBD	TBD	TBD	TBD	TBD
				2,526,300.00	-	14,796.50	138,119.50										
MHW Elevator 1-2 Modernization	Design	TBD	SALTZ MICHELSON ARCHITECTS	321,000.00	-	50,697.50	62,873.50	207,429.00	TBD	TBD	TBD	Bid	TBD	TBD	TBD	TBD	TBD
MHW MRI Upgrade	Construction	LEE CONSTRUCTION	HARVARD JOLLY INC	2,887,800.00	-	118,727.64	1,102,433.12	1,666,639.24	912,030.00	136,804.00	Yes	Bid	09/25/2024	03/31/2025	08/04/2025	Yes	On Schedule
MHW MCVI West*	Construction	LEE CONSTRUCTION	HARVARD JOLLY INC	10,300,000.00	4,727.18	303,796.83	9,849,234.89	142,241.10	5,699,505.00	854,925.00	Yes	Bid	12/04/2024	03/05/2025	10/31/2025	Yes	On Schedule
MHW MCI Infusion Expansion*	Permitting/Bidding	THORNTON CONSTRUCTION	HKS ARCHITECTS INC	2.685.600.00	-	238.962.04	148.663.69	2,297,974.27	1,984,552.00	297,000.00	Yes	Bid	02/27/2025	TBD	TBD	TBD	TBD
emorial Manor - 20		1															
Manor Generator/ATS Replacement*	Design	TBD	SALTZ MICHELSON ARCHITECTS	500,000.00	-	56,024.40	49,762.60	394,213.00	TBD	TBD	Yes	Bid	TBD	TBD	TBD	TBD	TBD
Manor Piped-in O2*	Permitting/Bidding	TBD	HKS ARCHITECTS INC	352,267.98		61,478.50	30,040.48	260,749.00	TBD	TBD	Yes	Bid	05/27/2025	TBD	TBD	TBD	TBD
Manor FEMA Hardening*	Permitting/Bidding	LEE CONSTRUCTION	SALTZ MICHELSON ARCHITECTS	3,250,000.00	165,843.43	116,148.14	142,004.37	2,826,004.06	4,217,850.00	632,000.00	Yes	Bid	02/27/2025	TBD	TBD	TBD	TBD
emorial Physicians Group - 80																	
/IHM MOB Suite 309 Maternal Fetal Medicine	Design	TBD	SALTZ MICHELSON ARCHITECTS	1,553,400.00	_	22,101.00	51,353.09	1,479,945.91	TBD	TBD	TBD	Bid	TBD	TBD	TBD	TBD	TBD
MPG MHW 603 Ste 250 Division of Urology*	Design	TBD	SALTZ MICHELSON ARCHITECTS	2.093.101.00		151.129.71	90.068.13	1,851,903.16	TBD	TBD	TBD	Bid	June (Tentative)	TBD	TBD	TBD	TBD
emorial Primary Care Regional - 640																	
Buildout Dania Beach Center	Construction	LEE CONSTRUCTION	SALTZ MICHELSON ARCHITECTS	3.120.300.00	71,589,80	1.091.877.81	1.428.764.29	528,068.10	1,915,242.00	287,000.00	Yes	Bid	03/27/2024	09/16/2024	06/26/2025	Yes	On Schedule
manial Damianal Hannital 40			ARCHITECTS	3,120,300.00	71,363.60	1,091,077.01	1,420,704.29										
emorial Regional Hospital - 40 MCI Hallandale Expansion*	Design	TBD	HARVARD JOLLY INC					4,143,206.05	TBD	TBD	Yes	Bid	05/27/2025	TBD	TBD	TBD	TBD
				4,337,400.00	-	63,790.45	130,403.50										
MRH Bi-Plane Upgrade (Neuro CVI)*	Permitting/Bidding	LEE CONSTRUCTION	GRESHAM SMITH SALTZ MICHELSON	1,400,000.00	-	113,815.06	1,932,093.56	-645,908.62	758,625.00	113,000.00	Yes	Bid	02/27/2025	TBD	TBD	TBD	TBD
MRH Linear Accelerator Equip	Design	TBD	ARCHITECTS SALTZ MICHELSON	5,085,100.00	270,455.73	4,348,169.94	22,096.94	444,377.39	TBD	TBD	TBD	Bid	TBD	TBD	TBD	TBD	TBD
MRH Service Elevators 1-2-3*	Permitting/Bidding	TBD	ARCHITECTS	1,800,000.00	-	65,243.75	23,056.25	1,711,700.00	TBD	TBD	TBD	Bid	TBD	TBD	TBD	TBD	TBD
MRH Kidney Transplant Clinic*	Construction	Landlord Fit Out	HARVARD JOLLY INC	2,950,000.00	-	133,103.03	46,085.27	2,770,811.70	TBD	TBD	Yes	BID	01/20/2025	TBD	10/25/2025	Yes	On Schedul
ER Renovation*	Construction	TURNER CONSTRUCTION	HARVARD JOLLY INC	20,759,500.00	9,660,510.08	4,884,866.04	3,925,821.02	2,288,302.86	16,401,716.00	1,922,604.00	Yes	GMP	05/25/2022	01/09/2023	12/25/2025	Yes	On Schedul
MRH Chiller Replacement*	Planning	TBD	DAVILA ENGINEERING	800,000.00	_		-	800,000.00	TBD	TBD	TBD	Bid	TBD	TBD	TBD	TBD	TBD
Master Plan Surgery & Tower*	Permitting/Bidding	ROBINS & MORTON	HKS ARCHITECTS INC			-	-	21,887,106.42	TBD	TBD	TBD	GMP	TBD	TBD	TBD	TBD	TBD
emorial Regional Hospital South - 41																	
MRHS Pedestrian Bridge Restoration	Permitting/Bidding	LEGO CONSTRUCTION	ASSOCIATES INC	500,000.00	-	30,800.00	23,200.00	446,000.00	1,688,315.20	253,000.00	Yes	Bid	02/27/2025	TBD	TBD	TBD	TBD
Chiller 3 Replacement	Construction	LEE CONSTRUCTION	SALTZ MICHELSON ARCHITECTS	2,430,000.00	173,453.37	573,022.49	1,024,821.14	658,703.00	1,456,277.00	218,000.00	Yes	Bid	04/26/2023	12/03/2024	06/30/2025	Yes	On Schedul
MRHS CT Imaging Suite Addition	Design	TBD	HARVARD JOLLY INC	1,250,000.00		58,031.79	73,064.21	1,118,904.00) TBD	TBD	TBD	Bid	June (Tentative)	TBD	TBD	TBD	TBD
HVAC AHU 3	Design	TBD	SALTZ MICHELSON		-			2,109,654.00		TBD	TBD	Bid	June (Tentative)	TBD	TBD	TBD	TBD
		THORNTON	ARCHITECTS HKS ARCHITECTS INC	2,198,400.00	1,560.00	58,370.00	28,816.00	2,100,004.00	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD	TBD
MRHS Remediation	Planning	CONSTRUCTION		n/a (new)													



MEMORIAL REGIONAL HOSPITAL • MEMORIAL REGIONAL HOSPITAL SOUTH • JOE DIMAGGIO OCHILDREN'S HOSPITAL MEMORIAL HOSPITAL WEST • MEMORIAL HOSPITAL MIRAMAR • MEMORIAL HOSPITAL PEMBROKE • MEMORIAL MANOR

TO:	Shane Strum, Interim President and Chief Executive Officer
FROM:	Mark Greenspan, Vice President Construction and Property Management
SUBJECT:	Bid Opening: Memorial Cancer Institute - Hallandale Expansion Memorial Manor – Piped-In Oxygen
DATE:	May 12, 2025

Bids for multiple projects were opened at 3:00 p.m. on May 12, 2025, in the Executive Conference Room. In attendance were Mr. Brad Friedman, Ms. Elizabeth Justen, Mr. Shane Strum, Mr. Irfan Mirza, Mr. Joseph Kadis, Mr. Kevin Wolkenfeld, Ms. Kim Paez, Mr. Pedro Arana, Mr. David Webb, Mr. Philoron Wright, Ms. Carmen Gonzalez, and Mr. Mark Greenspan, along with representatives from Engel Construction, Inc., Lee Construction Group, Inc., Lego Construction Co., and Thornton Construction Company, Inc.

Bids for the Memorial Cancer Institute - Hallandale Expansion, and Memorial Manor – Piped-In Oxygen were received:

Memorial Cancer Institute - Hallandale Expansion

\triangleright	Engel Construction, Inc.	\$5,883,501.14
\succ	Lee Construction Group, Inc.	\$4,503,870.00
\succ	Lego Construction Co.	\$7,871,900.40
\succ	Thornton Construction Company, Inc.	\$3,829,402.01
Mem	<u>orial Manor - Piped-In Oxygen</u>	
<u>Mem</u> ≻	orial Manor - Piped-In Oxygen Engel Construction, Inc.	\$1,780,725.45
<u>Mem</u> ≻ ≻		\$1,780,725.45 \$1,225,245.00
Mem	Engel Construction, Inc.	
Mem	Engel Construction, Inc. Lee Construction Group, Inc.	\$1,225,245.00

Mr. Greenspan informed the group, as has been the standard practice, that the bids would be reviewed and verified for accuracy.

Recommendations for award will be presented at the next regularly scheduled Board Building Committee Meeting.
